




Report VTC 20th of January 2014

- 1 Storage Room
- 2 Kitchen and Restaurant
- 3 Classroom 1
- 4 Classroom 2
- 5 Classroom 3
- 6 Classroom 4
- 7 Sanitary Girls
- 8 Boarding Girls 1
- 9 Boarding Girls 2
- 10 Computerroom
- 11 Library 1
- 12 Library 2
- 13 Administration 1
- 14 Administration 2
- 15 Administration 3
- 16 Sanitary Boys
- 17 Boarding Boys 1
- 18 Boarding Boys 2
- 19 Practical 1
- 20 Practical 2
- 21 Practical 3
- 22 Practical 4
- 23 Practical 5
- 24 Carpentry Workshop
- 25 Auto mechanics Workshop
- 26 Auditorium
- 27 Classroom 5
- 28 Classroom 6
- 29 Classroom 7
- 30 Classroom 8
- 31 Teachers Houses
- 32 Piggery
- 33 Poultry
- 34 Laboratory & Waterbassin
- 35 Cattle shed

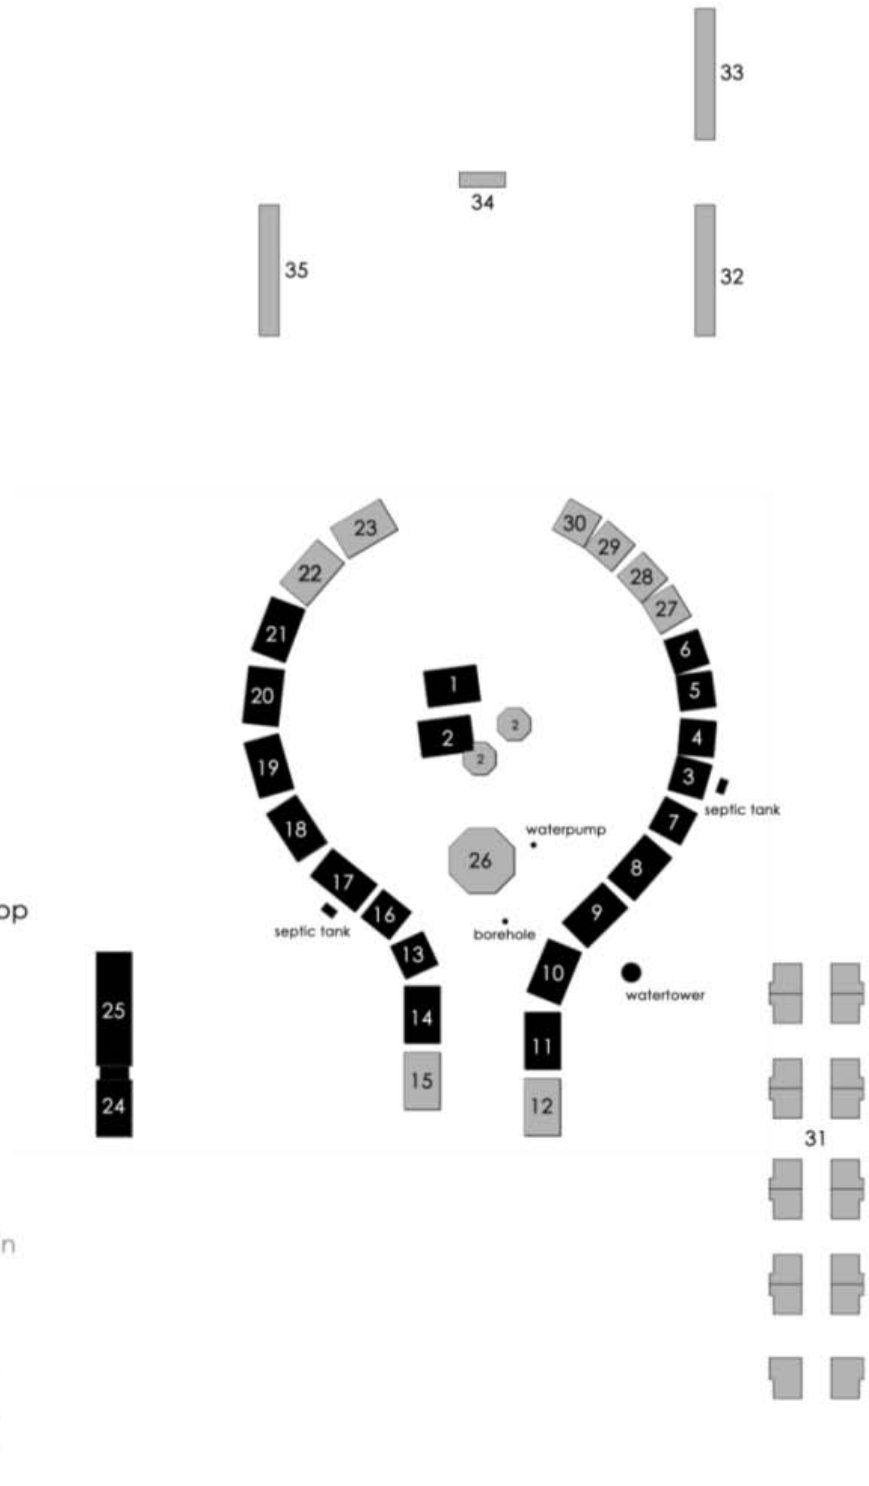

Phase 1

Phase 2

Dear members GKMT,

Following you'll find the monthly report on the activities at the VTC.

Buildings 6, 5, 4, 3 and 7. Some reparations on the thatched roofs, just minor issues, not leakages. Except for painting and installations and tiles in the sanitary block, these buildings are finished.

8 Boarding Girls 1. Assembled and fixed a demo ceiling in one of the bedrooms. The purpose of the ceiling is threefold. Firstly it avoids or at least discourages theft by climbing over the walls. Secondly the idea was to reduce noise disturbance between rooms, although it seems not to give the desired effect and thirdly the ceiling takes away the sense of sleeping in a barn. We chose for an open ceiling because otherwise we would lose the natural ventilation which occurs in the top of the building (↓). Except for the remaining ceilings and painting this building is finished.



9 Boarding Girls 2. Finished covering the ventilation triangles, assembled and fixed all the doors (interior and exterior), fixed the window glasses (↑). Except for the floor, cable boxes, ceilings and painting this building is finished.

10 Computerroom. Assembled and fixed the exterior doors front and back and fixed the window glasses. Finished door- and windowsills (↓). Except for the floor, cable boxes and painting this building is finished.



11 Library 1. Assembled and fixed the exterior doors front and back and fixed the window glasses. Finished door- and windowsills (↑). Except for the floor, cable boxes and painting this building is finished.

13 Administration 1. Fixed the window glasses and finished windowsills (↓).



14 Administration 2. Fixed the window glasses and finished windowsills (↑). Finished covering and started on ventilation triangles (↓).



17 Boarding Boys 1. Finished ring beam interior masonry (↑).



18 Boarding boys 2. Finished plastering the foundation box and pouring the floor slab. Started with masonry upper structure (↓).

Veranda. On the girl's wing, at the back side of the veranda we finished pouring the concrete slab for the gutter, the single layer brick wall and plastering the veranda wall (↑).

Terrain. Finished backfilling the ground between the walking paths of the veranda and leveling the terrain near the gutter at the front (↓).



VTC Football Team. The Dutch foundation "[Football Maties](#)", a non-profit organization from Arnhem, collects football shoes and materials in the Netherlands to support organizations in African countries with their sports programs. They approved our project and sponsored the VTC team with 60 pairs of brand new shoes of which 37 pairs have arrived to Mpongwe in my luggage. The remaining amount is yet to come. After deliberating with the founder of Football Maties we decided to leave open the possibilities for future cooperation. So far, ideas are assisting GCMF with the construction of the sports field or sending professional Dutch volunteer trainers to give training courses to local trainers in Mpongwe.



Plot number. As you have been reading in my last report, there were some issues over a couple of pieces of land purchased by GCMF in the past. I made a proposal for the two families involved and recently signed a trading contract with Mr. Milambo. This new contract nullifies the three former contracts and solves the issue of the needlessly purchased piece within our own plot. There were no financial transactions concerned with this contract.

Tomorrow we start the negotiations about the left side with the Kafweni family.



Give the Children of Mpongwe a Future (GCMF)

Registered in Zambia as a society – number ORS/102/96/102

P.O. Box 14, Mpongwe



Mpongwe, December 2013

RE: CONTRACT - SELLING LAND TO GCMF

This contract is between **Mr. DONALD MILAMBO** and the **GCMF MANAGEMENT**. After a peaceful agreement I wish to declare the following:

I, Donald Milambo, hereby declare I sold **3,5 HECTARES** of land, located In Mpongwe District with the UTM coordinates as shown in the map below, to the foundation Give the Children of Mpongwe a Future (GCMF).

For this I received the amount of **KR 3800,00** (Three Thousand Eight Hundred Zambian Rebased Kwacha)

I am aware that this means I no longer have the right of owning this land and I transfer these rights to the GCMF.

Agreeing with the above mentioned terms this contract is signed by:

Mr. D. Milambo
Seller




Mr. A. B. Kalima
Chairman GCMF




Mr. A. B. Sol
Projectmanager GCMF



Mr. M. Kachingwe
Director of works, Council Mpongwe



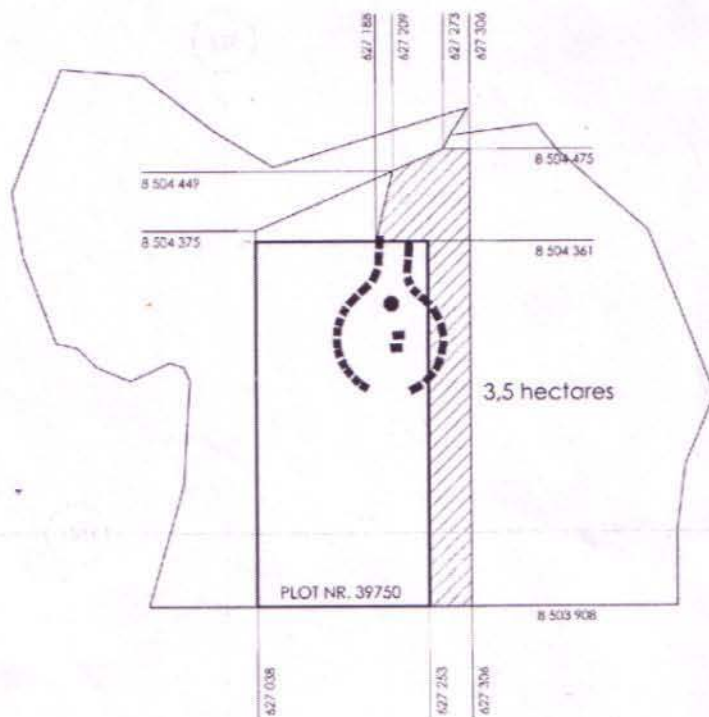

Kind regards, Bram
